

- Duration range
2 to 10 wks.

- Show all external
restraints on separate
sheet from activities of
THE

X indicates external
restraints on THE
work over which THE
has no control


- Responsibility Codes
- 99 THE
 - 1 AEPSC
 - 2 THE
 - 3 IME
 - 4 Bldg trade groups
 - 5 Midwest (MWS)
 - 6 Stanley Electric (SEC)
 - 7 Glant
 - 8 Peermc Cantey


MONITORING RECORD			ISSUE RECORD	
DATE	DATE	DATE	ISSUE No.	DATE
			1	OCT 1, 81
			2	-
			3	-
			4	OCT 20, 81
			5	DEC 14, 81

Reserved Note No.

NETWORK MODEL FOR
THE WORK
BREED PLANT PRECIPITATOR
PROJECT - FAIRBANKS
INDIANA

RALPH J. STEPHENSON, P.E.
15064 WARWICK ROAD
DETROIT, MICHIGAN 48223
CONSULTANT PH 273-5026



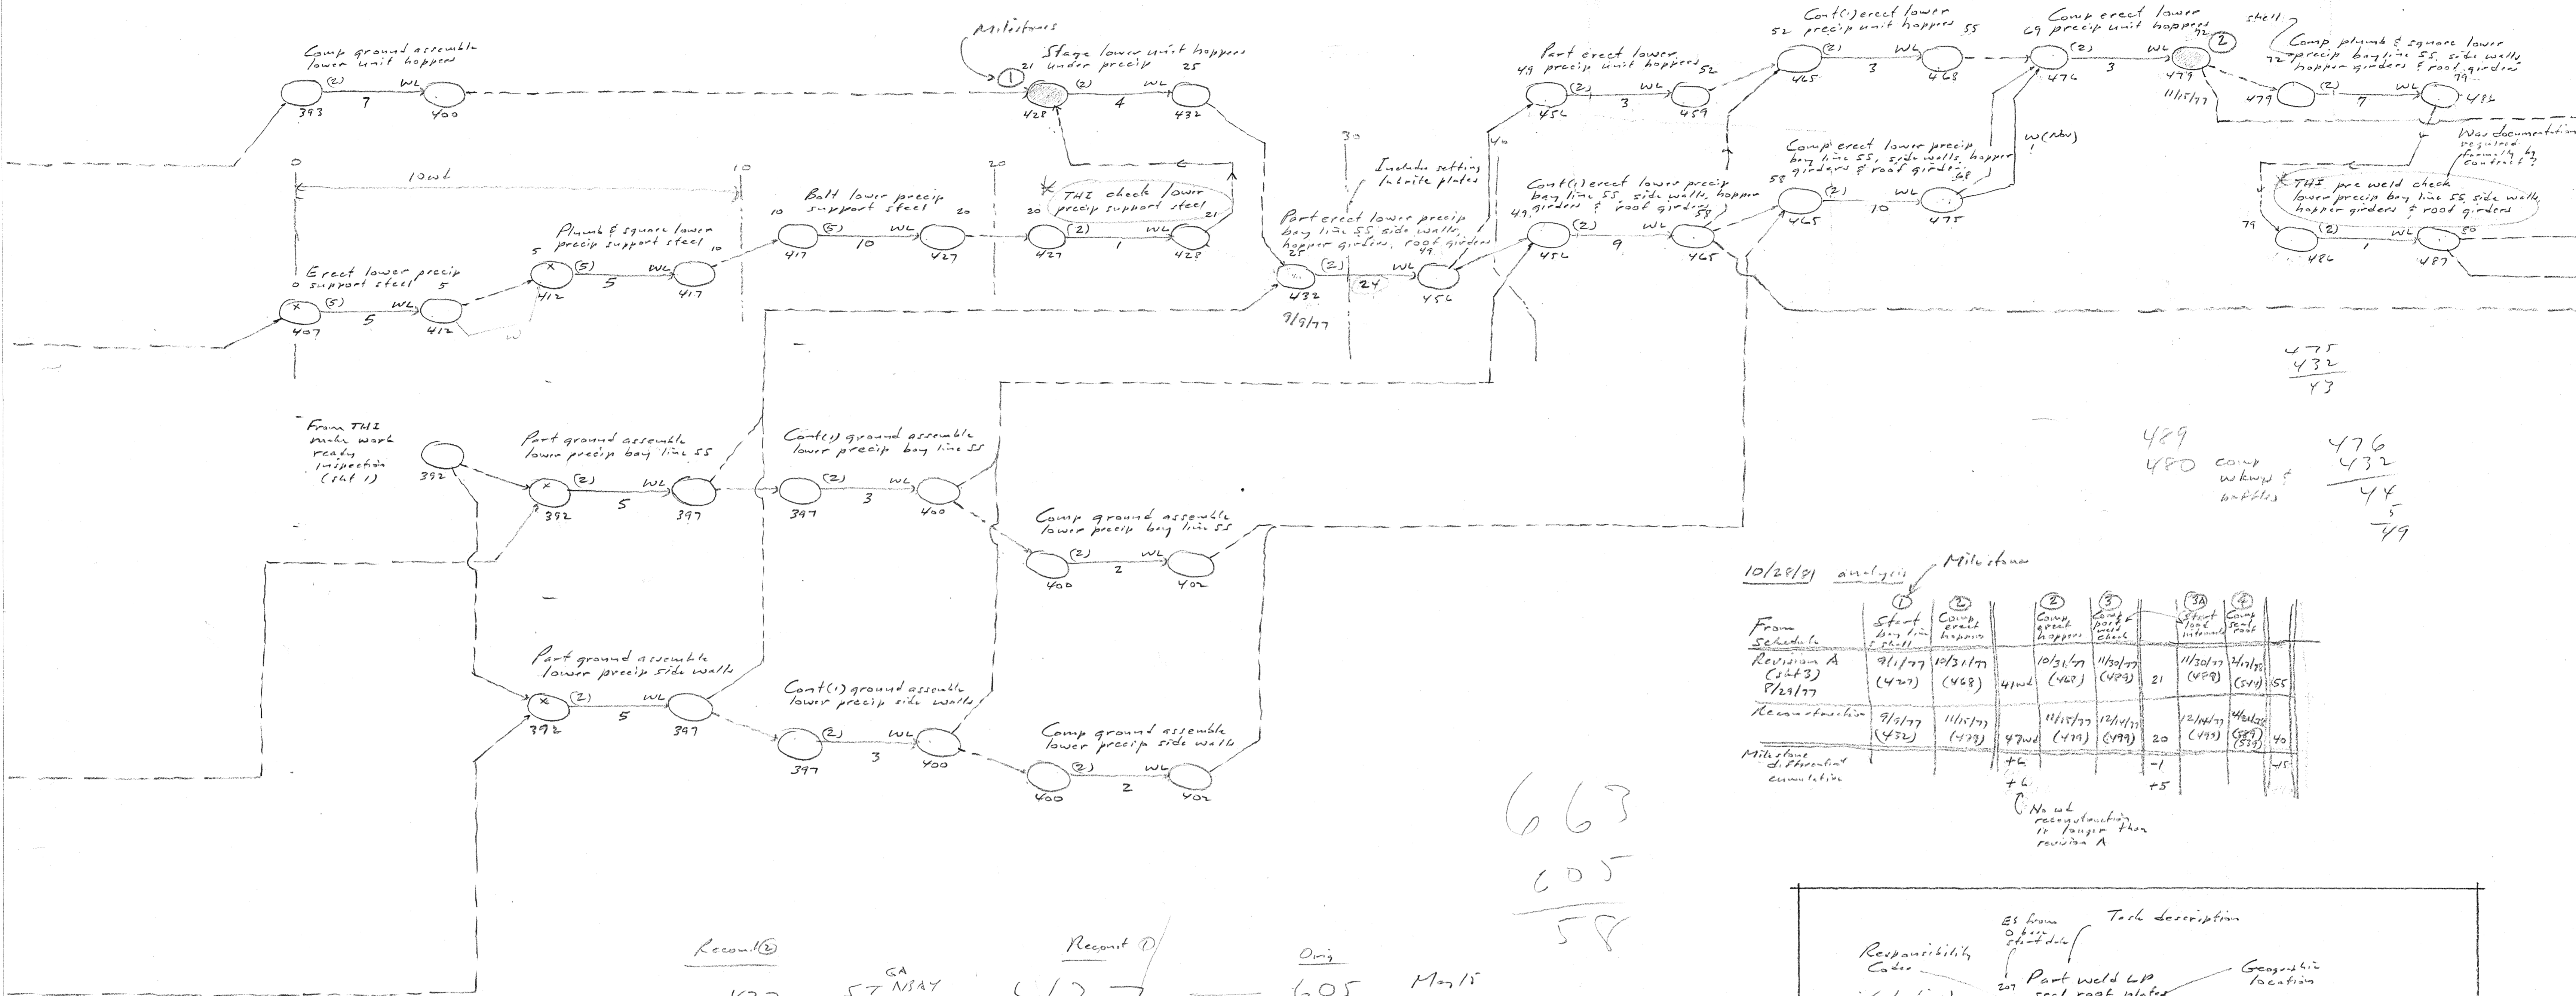

10/28/77 analysis Milestone


From Schedule	1	2	3	3A	4
Revision A (5143) 8/29/77	9/1/77 (427)	10/31/77 (468)	10/31/77 (468)	11/30/77 (477)	12/1/77 (511)
Reconstruction	9/1/77 (432)	11/1/77 (477)	11/1/77 (477)	12/1/77 (499)	1/1/78 (533)
Milestone of Present cumulative		+6	+6	-1	+5

No. w/L reconstruction is longer than revision A

Recon (E)	CA	Recon (P)	Orig	Milestone
427	57 MAY LINE SS	427	605	May 15
432	START ERECT MAY LINE SS	432	610	May 22
456	START ERECT HOPPERS	456	619	Jun 5
475	COMP ERECT MAY LINE SS	475	653	Jun 24
477	COMP ERECT HOPPERS	477	656	Jul 27
485	COMP PLUMB	485	663	Aug 7
58		48	58	
59		49	59	

WEATHER

Year	Month	Days	Notes
1907	AUG	0	JAN 2 (511)
1927	SEPT	0	FEB 1 (532)
1947	OCT	0	MAR 1 (552)
1967	NOV	1	APR 2 (573)
1977	DEC	1	MAY 1 (594)
			JUN 0 (617)
			JUL 0 (639)
			AUG 0 (659)
			SEP 0 9 (682)
			OCT 0 (702)
			NOV 1 (724)
			DEC 1 (745)
			JAN 2 (765)
			FEB 1 (787)
			MAR 1 (807)
			15

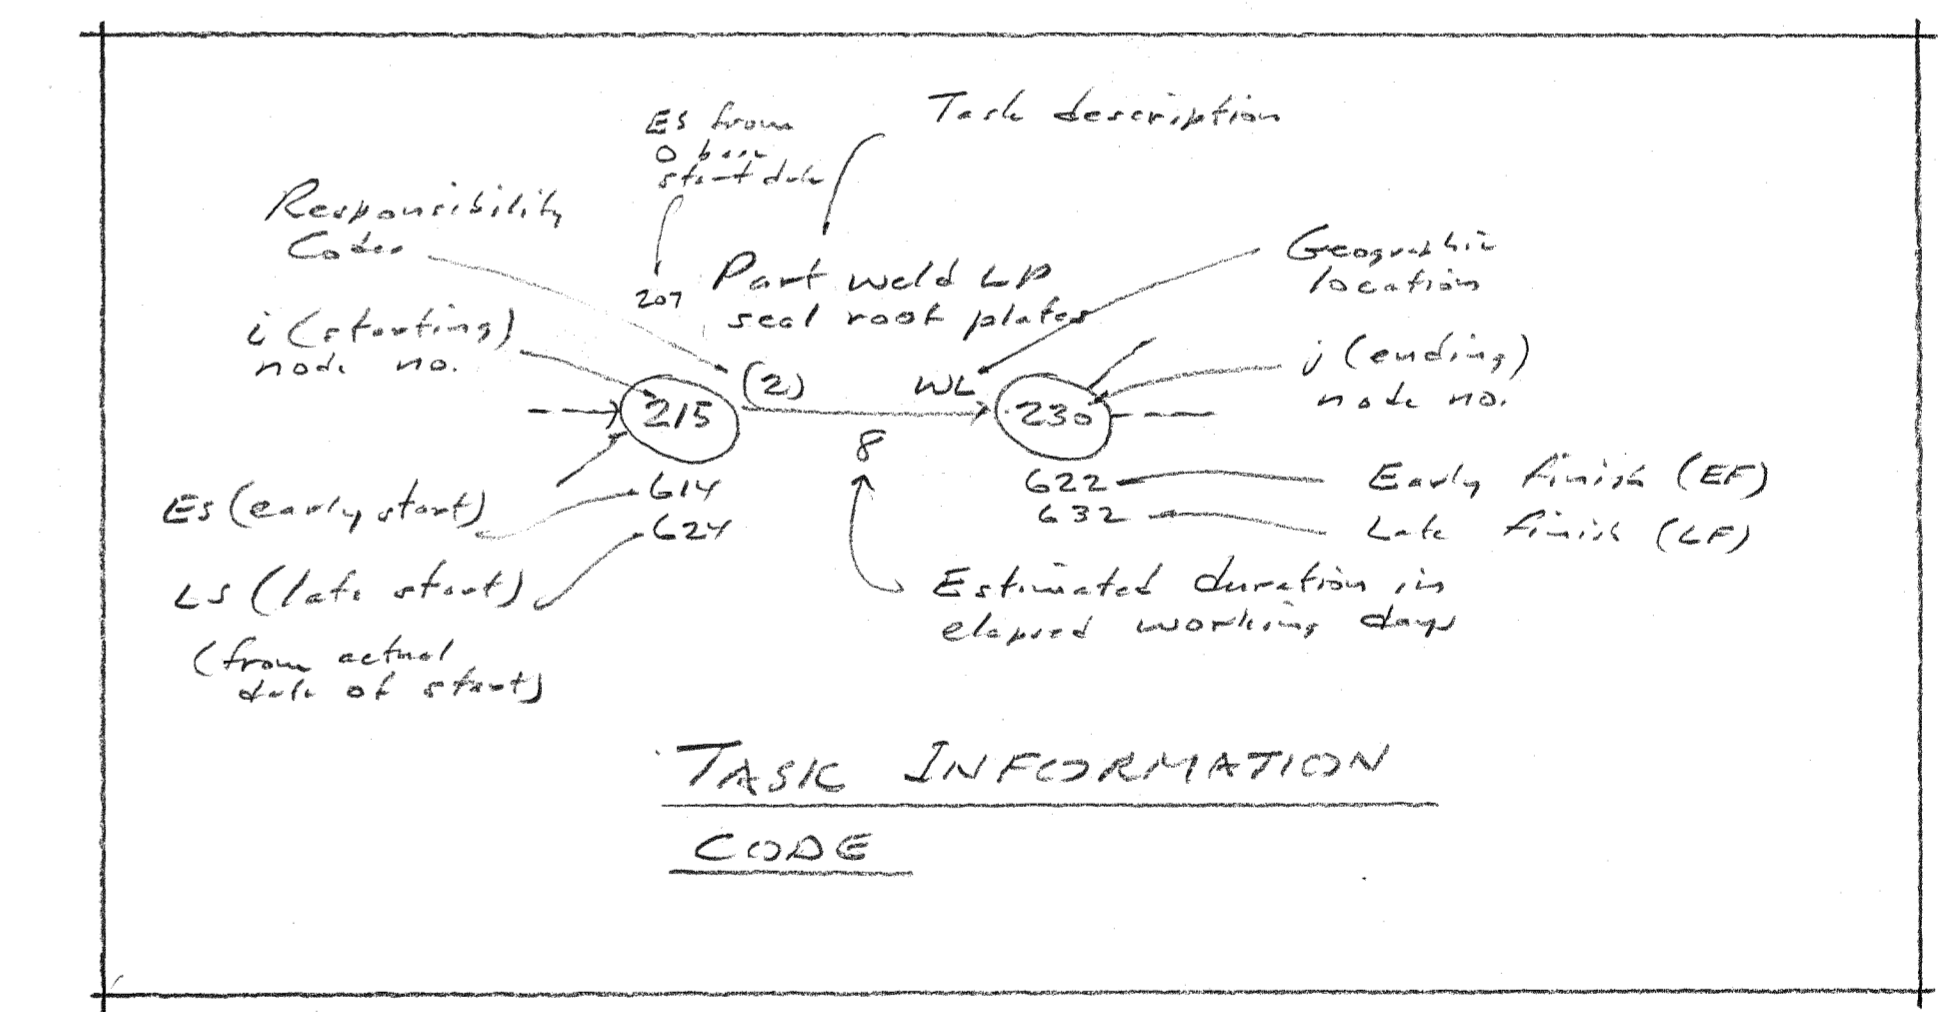

MONITORING RECORD			ISSUE RECORD	
DATE	DATE	DATE	ISSUE NO.	DATE
			1	Oct 1, 81
			2	Oct 2, 81
			3	-
			4	Oct 29, 81
			5	Oct 29, 81


Reserved Node Nos.

LN
NN

NETWORK MODEL FOR
THE WORK
BRED PLANT PRECIPITATOR
PROJECT - FAIRBANKS
INDIANA

RALPH J. STEPHENSON, P.E.
15064 WARWICK ROAD
DETROIT, MICHIGAN 48223
CONSULTANT PH 273-5026

2

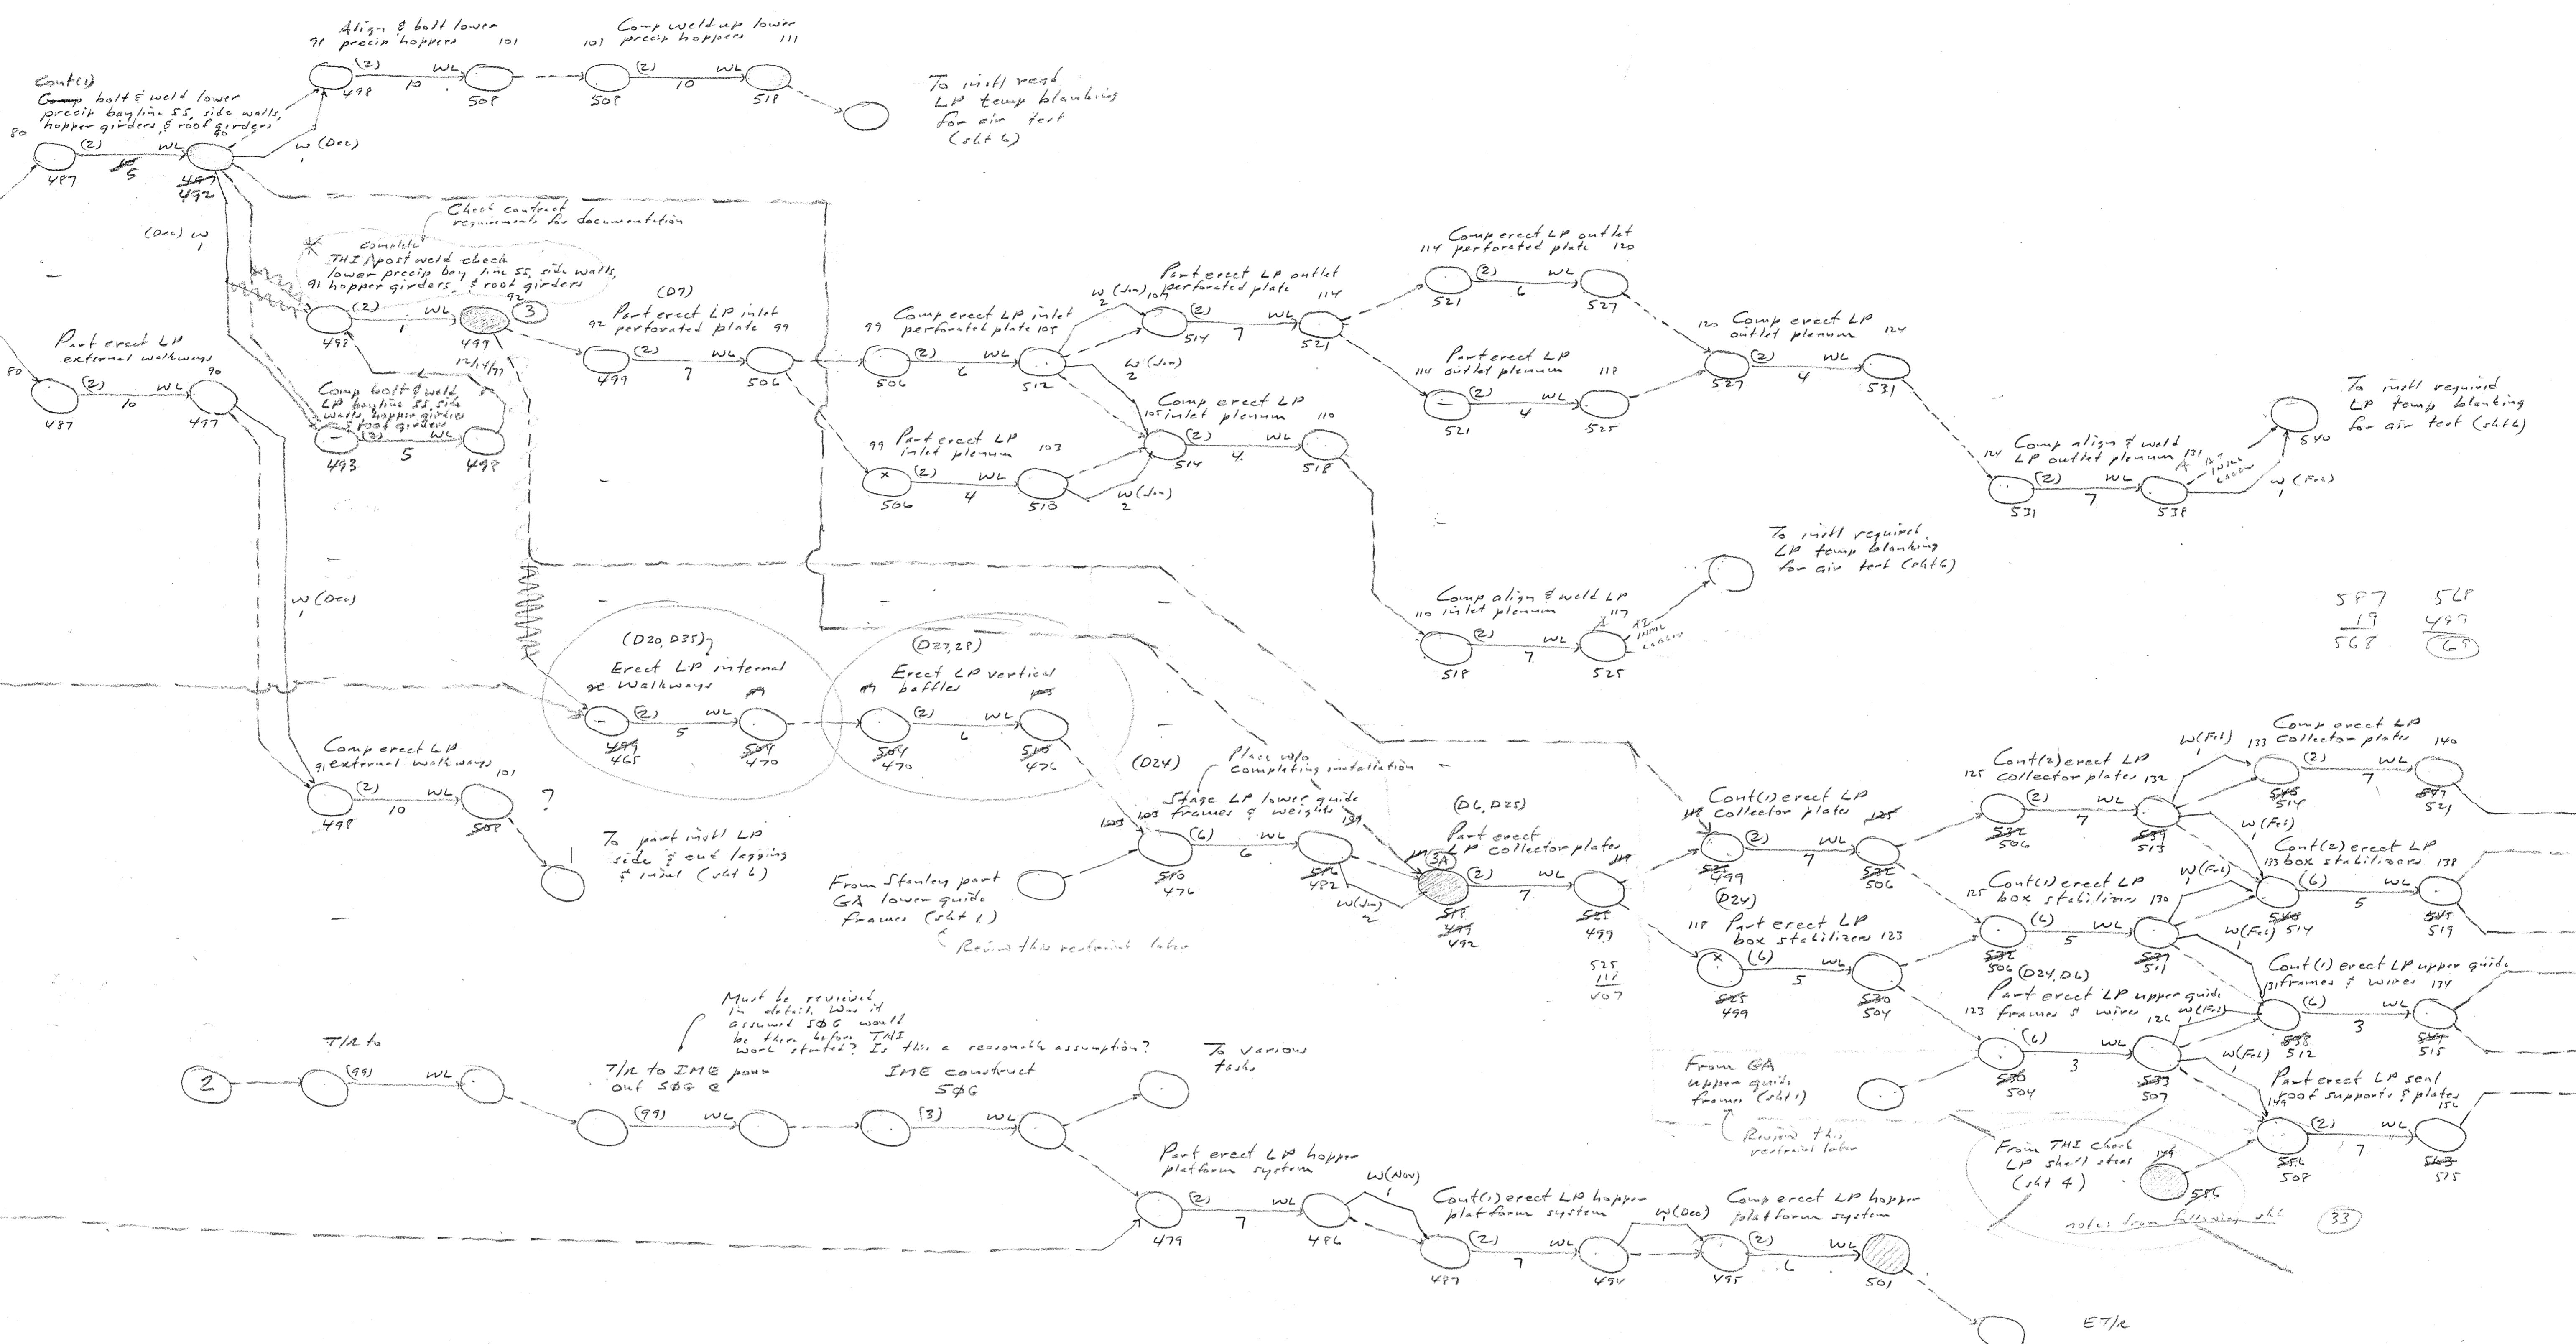

5F7 5LF
 19 425
 5G8 6

To part install LP side & end lagging & inlets (slit 4)

IME construct 5G6
 T/IL to IME pan out 5G6 e
 T/IL to

Must be reviewed in detail. Was it assumed 5G6 would be there before THI work started? Is this a reasonable assumption?

To various tasks

MONITORING RECORD			ISSUE RECORD	
DATE	DATE	DATE	ISSUE NO.	DATE
			1	Oct 1, 81
			2	Oct 8, 81
			3	Oct 14, 81
			4	Oct 20, 81
			5	Oct 28, 81

Reserved No. Nov.

NETWORK MODEL FOR
 THE WORK
 BREED PLANT PRECIPITATOR
 PROJECT - FAIRBANKS,
 INDIANA

RALPH J. STEPHENSON, P.E.
 15064 WARWICK ROAD
 DETROIT, MICHIGAN 48223
 CONSULTANT PH 273-5026

From THZ to deliver full contract to THZ (cont 1)

THZ to Midwest start work on interim SS

Stake out intermediate support steel

Part erect intermediate support steel

Cont(1) erect intermediate SS

Cont(2) erect intermediate SS

Comp erect intermediate SS

From Schedule	(5)	(6)	
Revision A 8/29/77	3/17/78 (564)	4/3/78 (575)	11
Reconstruction Item 4	4/10/78 (587)	7/14/78 (647)	60
Reconstruction Item 5	(589)	(599)	60

587
539
45

To part erect LP seal roof supports & plates (cont 2) make in proceeding order

THZ check LP shell

149 steel

(2) WL

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

555 556

28
31
16
47

587
578
69
499
488

Define check

180

587
432
155

587
432
155

30

587
428
159

642

159 from check of WIP to comp seal roof to support plates
30
76
265

RECONSTRUCTION WL 8:21

MONITORING RECORD			ISSUE RECORD	
DATE	DATE	DATE	ISSUE No.	DATE
			1	Oct 1, 81
			2	Oct 8, 81
			3	Oct 14, 81
			4	Oct 22, 81
			5	Oct 28, 81


Reserved Make Nos.

NETWORK MODEL FOR
THE WORK
Breed Plant Precipitator
PROJECT - FAIRBANKS,
INDIANA

RALPH J. STEPHENSON, P.E.
15064 WARWICK ROAD
DETROIT, MICHIGAN 48223
CONSULTANT PH 273-5026

4

LW
HW

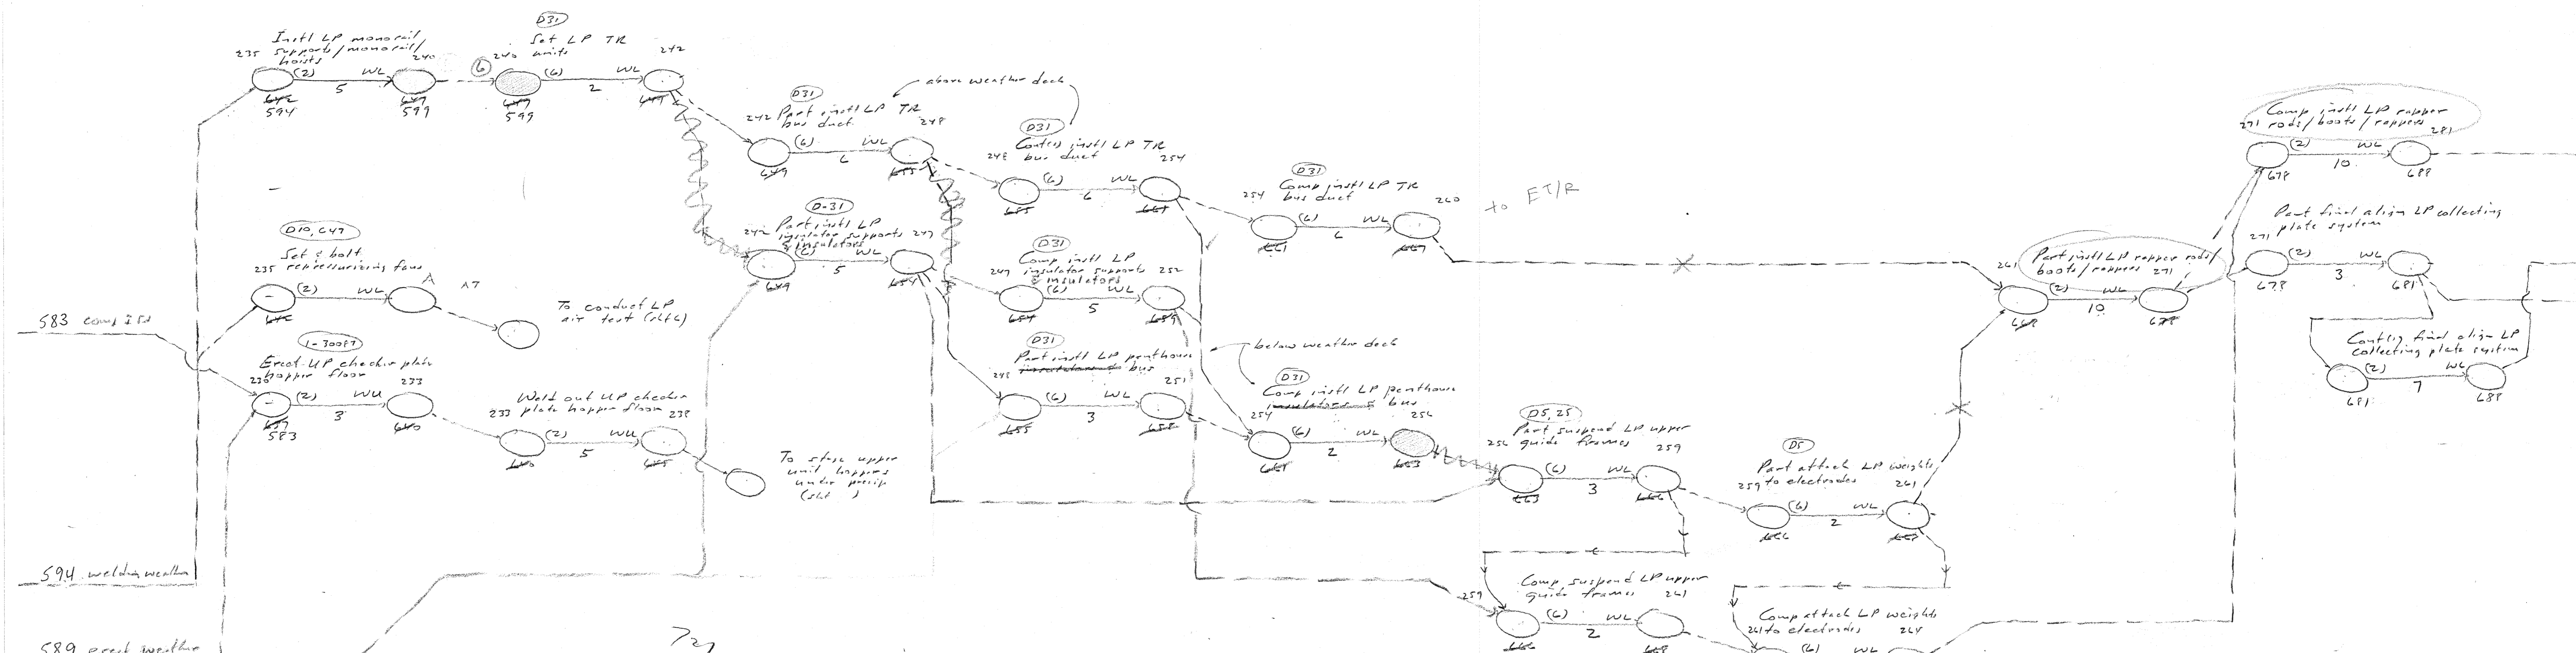

From Schedule			
Revision A (11/3)			
Reconst Issue 4			
Reconst Issue 5			


RECONSTRUCTION WL 81:21

MONITORING RECORD			ISSUE RECORD	
DATE	DATE	DATE	ISSUE NO.	DATE
			1	
			2	Oct 9, 91
			3	Oct 14, 91
			4	Oct 29, 91
			5	Oct 28, 91


Reserved Node Nos

NETWORK MODEL FOR
 THE WORK
 BREED PLANT PRECIPITATOR
 PROJECT - FAIRBANKS

INDIANA
 RALPH J. STEPHENSON, P.E.
 15064 WARWICK ROAD
 DETROIT, MICHIGAN 48223
 CONSULTANT PH 273-5026



LN
HN

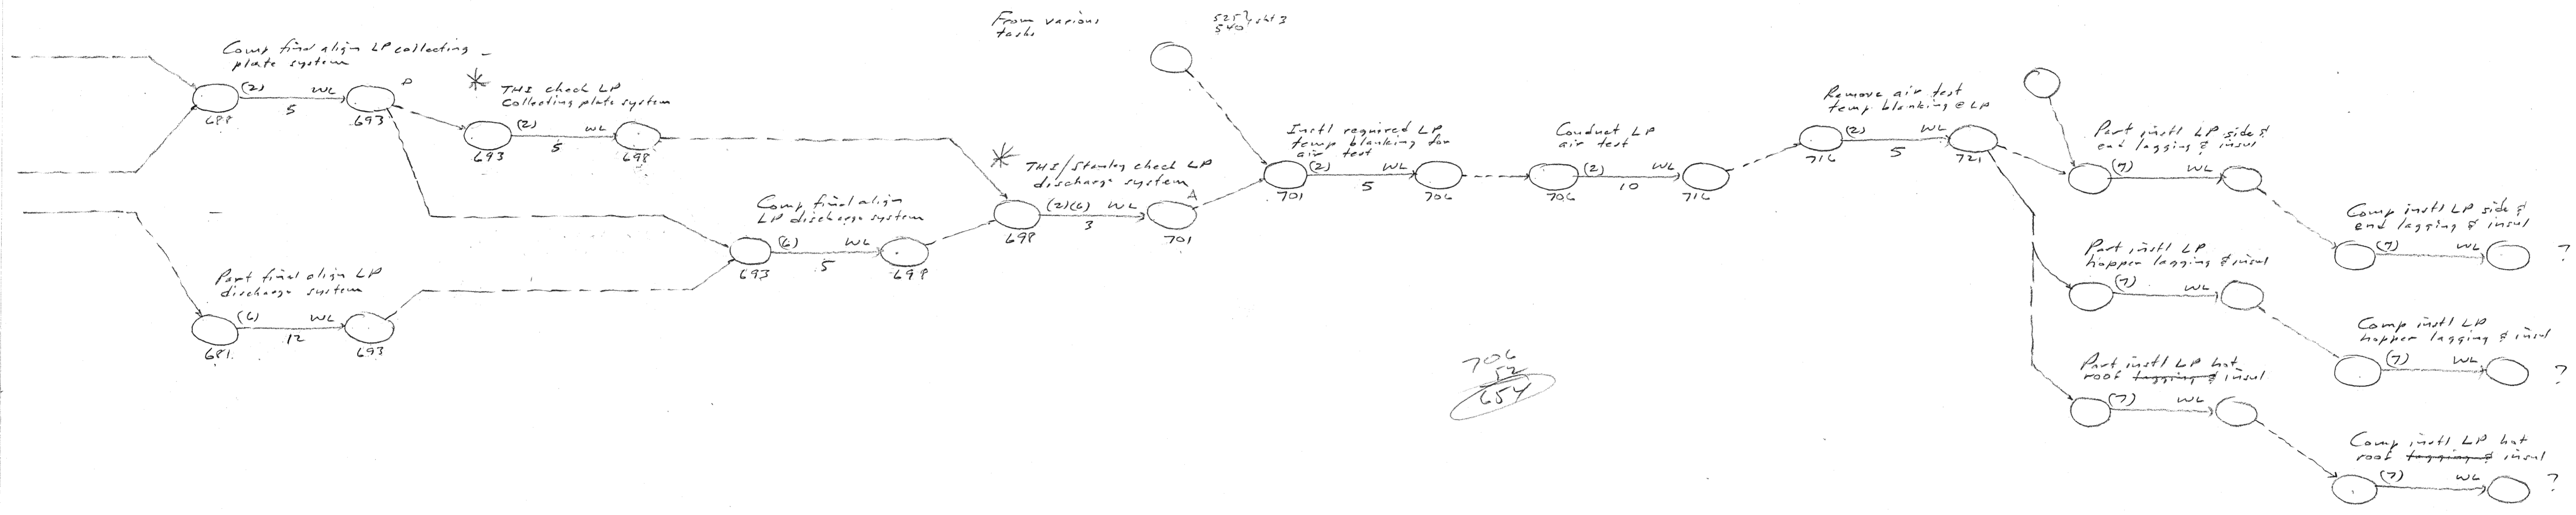

706
12
654

RECONSTRUCTION WL

81:21

MONITORING RECORD			ISSUE RECORD	
DATE	DATE	DATE	ISSUE No.	DATE
			1	-
			2	0678.P1
			3	0674.P1
			4	0678.P1
			5	0678.P1

Revised 10/2/81

NETWORK MODEL FOR
THE WORK
BREED PLANT PRECIPITATION
PROJECT - FAIRBANKS

INDIANA
RALPH J. STEPHENSON, P.E.
15064 WARWICK ROAD
DETROIT, MICHIGAN 48223
CONSULTANT PH 273-5026

6

LH
HX
