
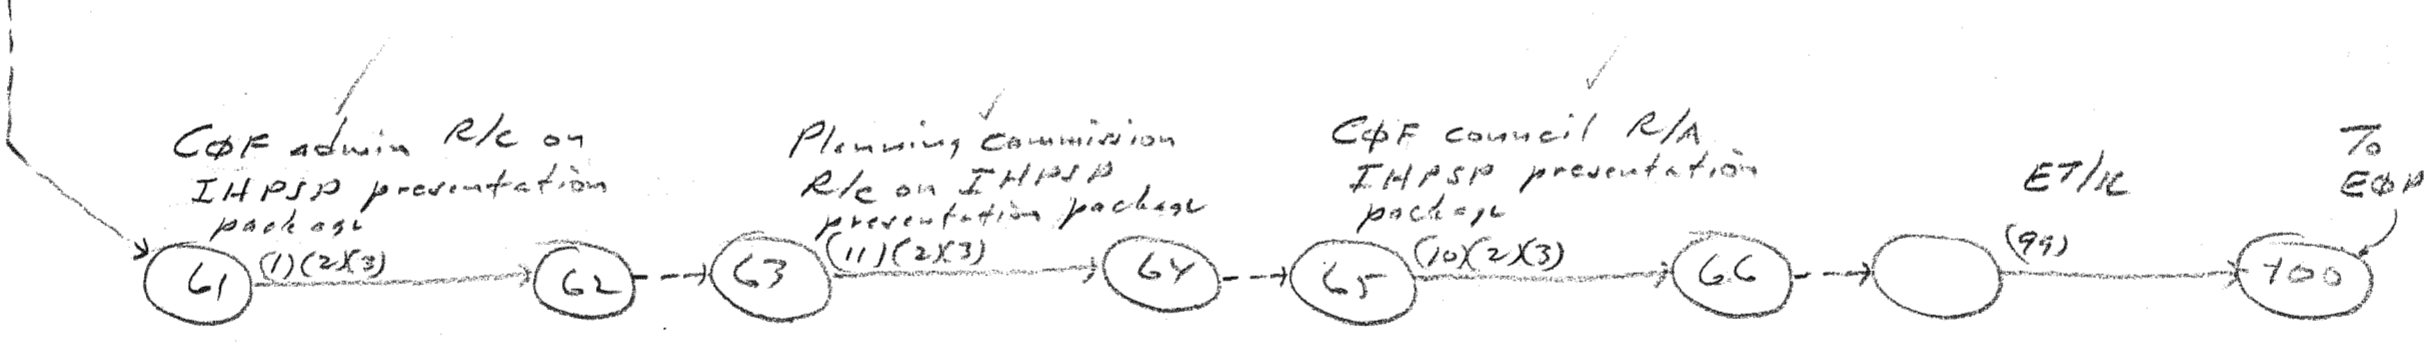


Conceptual Preliminary Schedule

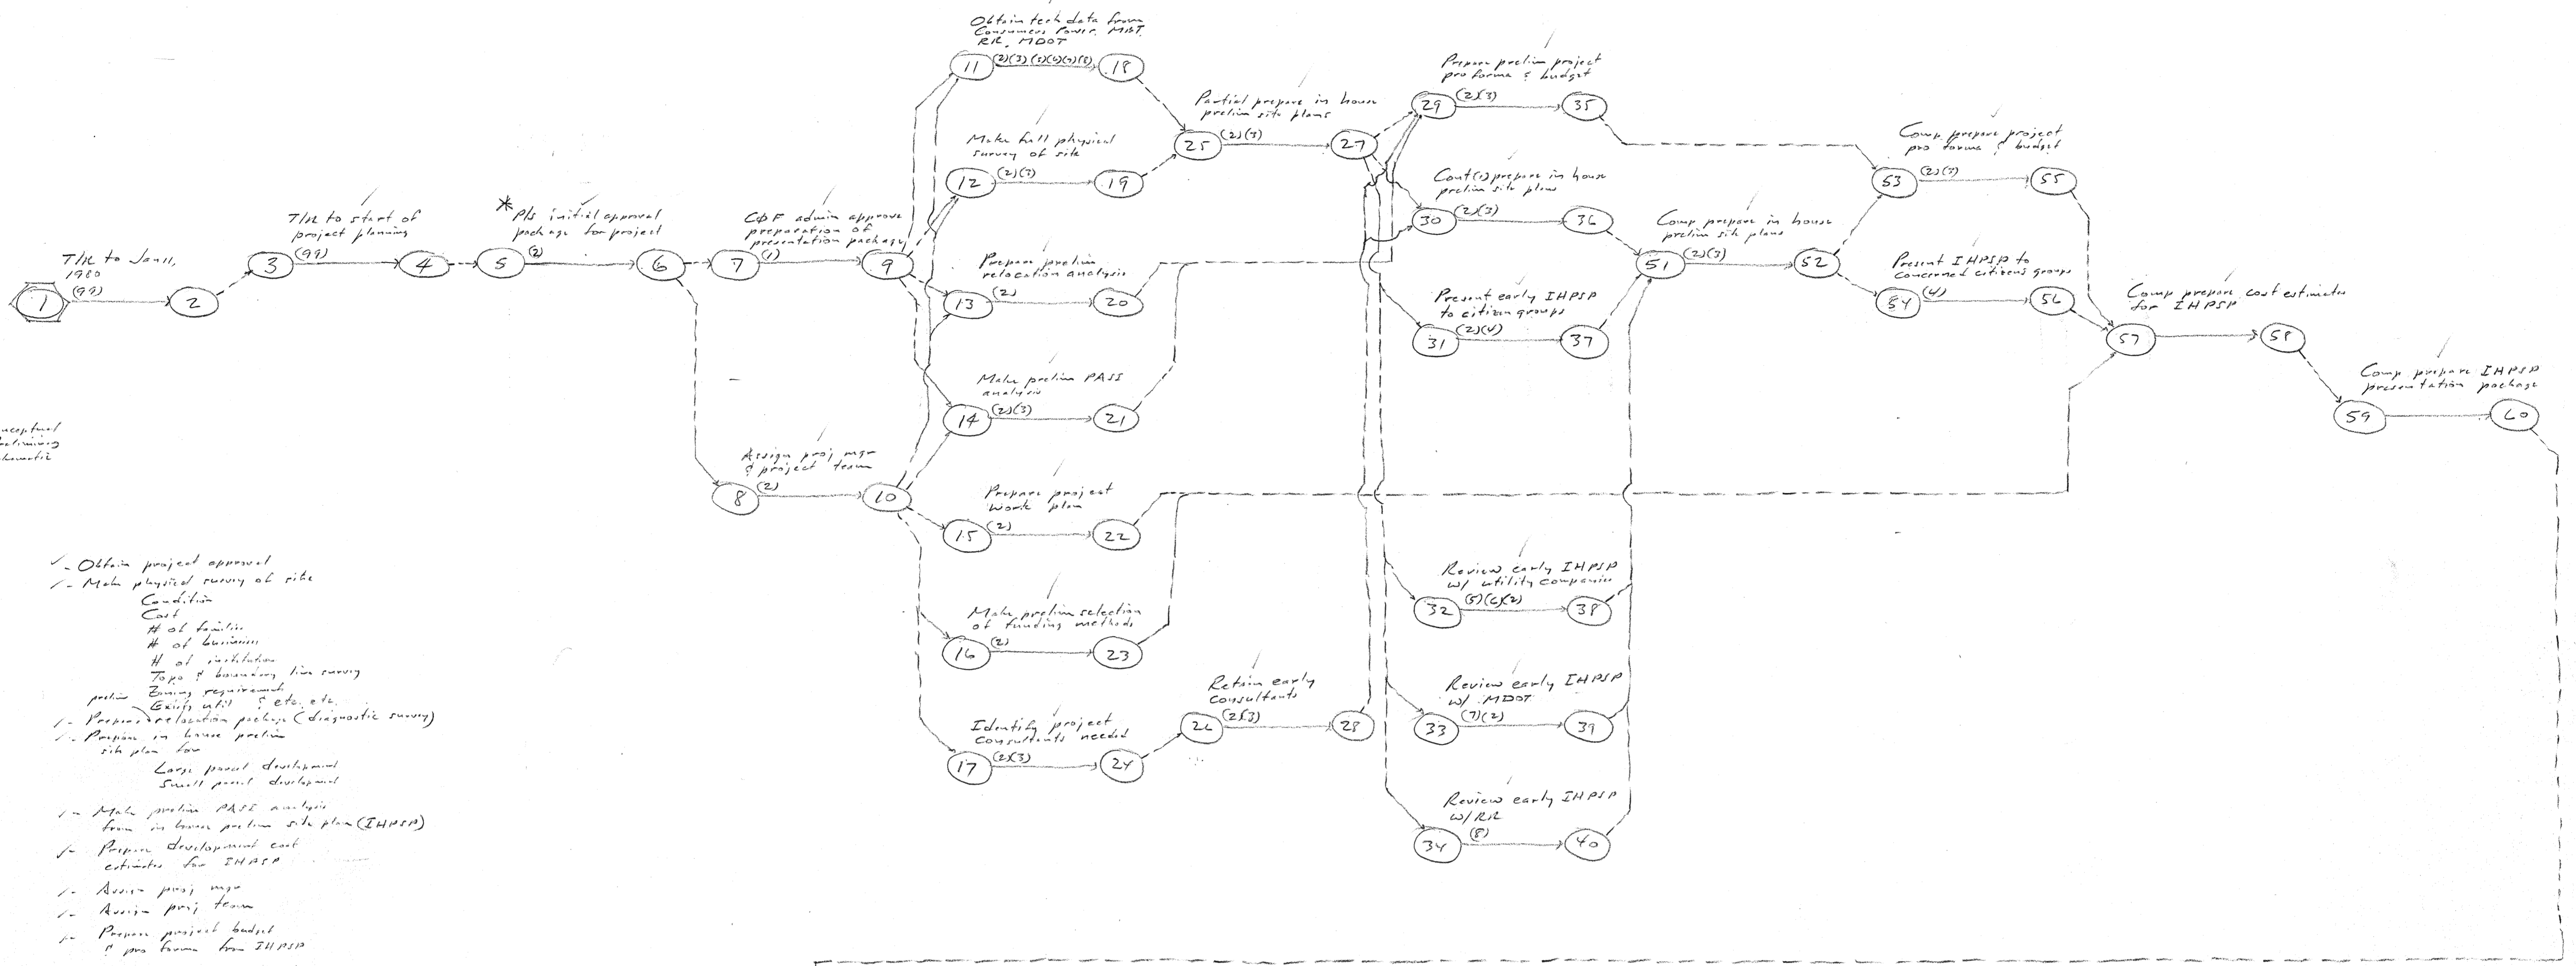

- Obtain project approval
- Make physical survey of site
 - Condition
 - Cost
 - # of families
 - # of business
 - # of institutions
 - Types of business line survey
 - zoning requirements
 - Existing utility & etc. etc.
- Prepare relocation package (diagnostic survey)
- Prepare in house preliminary site plan for
 - Large parcel development
 - Small parcel development
- Make preliminary PASE analysis from in house preliminary site plan (IHPSIP)
- Prepare development cost estimates for IHPSIP
- Assign project mgr
- Assign project team
- Prepare project budget & pro forma for IHPSIP
- Prepare project work plan
- Prepare presentation package for IHPSIP
- Mayor R/A IHPSIP presentation
- Council R/A IHPSIP
- Select methods of funding
- MDT & CP R/C IHPSIP
- S&M D&T R/C IHPSIP
- RR R/C IHPSIP
- Obtain data from CP, MDT, RR & DOT for planning
- Obtain _____ grants or applicable
- Obtain _____ funding as applicable

- Responsibilities**
- 1 City of Flint administration
 - 2 DCD
 - 3 DAW
 - 4 Citizen groups
 - 5 Consumers Town
 - 6 Michigan Bell Telephone
 - 7 MDOT
 - 8 Railroads (RR)
 - 9 Consultants
 - 10 City of Flint council
 - 11 Planning Commission
 - 12 George Urey

General Notes

* indicates several methods for doing this activity as available.

- Abbreviations**
- IHPSIP In house preliminary site plan
 - T/R Time restraint
 - CP Consumers Power
 - M&T Michigan Bell Telephone
 - P/S Prepare/submit
 - R/A Review & approve
 - R/C Review & comment
 - RR Railroad
 - MDOT Michigan Department of transportation
 - ET/R End time restraints

MONITORING RECORD			ISSUE RECORD	
DATE	DATE	DATE	ISSUE No.	DATE
			1	JAN 19 80
			2	JAN 21 80
			3	FEB 25 80

- Reserved Node Nos.**
- 41 46
 - 42 47
 - 43 48
 - 44 49
 - 45 50

LH 1
HN

NETWORK MODEL FOR
SAMPLE INDUSTRIAL DEVELOPMENT
FLINT, MICHIGAN
CASE STUDY FOR GENERATING
STANDARD IMPLEMENTATION PROCEDURES #049

RALPH J. STEPHENSON, P.E.
15064 WARWICK ROAD
DETROIT, MICHIGAN 48223
CONSULTANT PH 273-5026

CS-1
