

- 4/1/72
- Summary list
- ✓ HRC prepare final alignment layout
 - ✓ Plc easement document
 - ✓ HRC design document
 - ✓ HRC R/A R/A easement document
 - ✓ Interim site survey route #7 w/ contractor
 - Plc bulletin for route #7
 - Price route #7 revision
 - Issue change order for #7
 - Plc DNR package for R/A (schematic proposal)
 - Submit change order to DNR
 - DNR R/A change order
 - CAF execute CO for #7
 - Authorize construction of #7

MONITORING RECORD			ISSUE RECORD	
DATE	DATE	DATE	ISSUE No.	DATE
			1	Nov 13, 71
			2	-
			3	-
			4	DEC 22, 71
			5	JAN 6, 72

Reserved Note Nos.

LW
HN

NETWORK MODEL FOR
TUNNEL ROUTE ALTERNATE
ACTION
FLINT, MICHIGAN


#094
#086

RALPH J. STEPHENSON, P.E.
15064 WARWICK ROAD
DETROIT, MICHIGAN 48223
CONSULTANT PH 273-5026

60

244
260
304

259
223
304

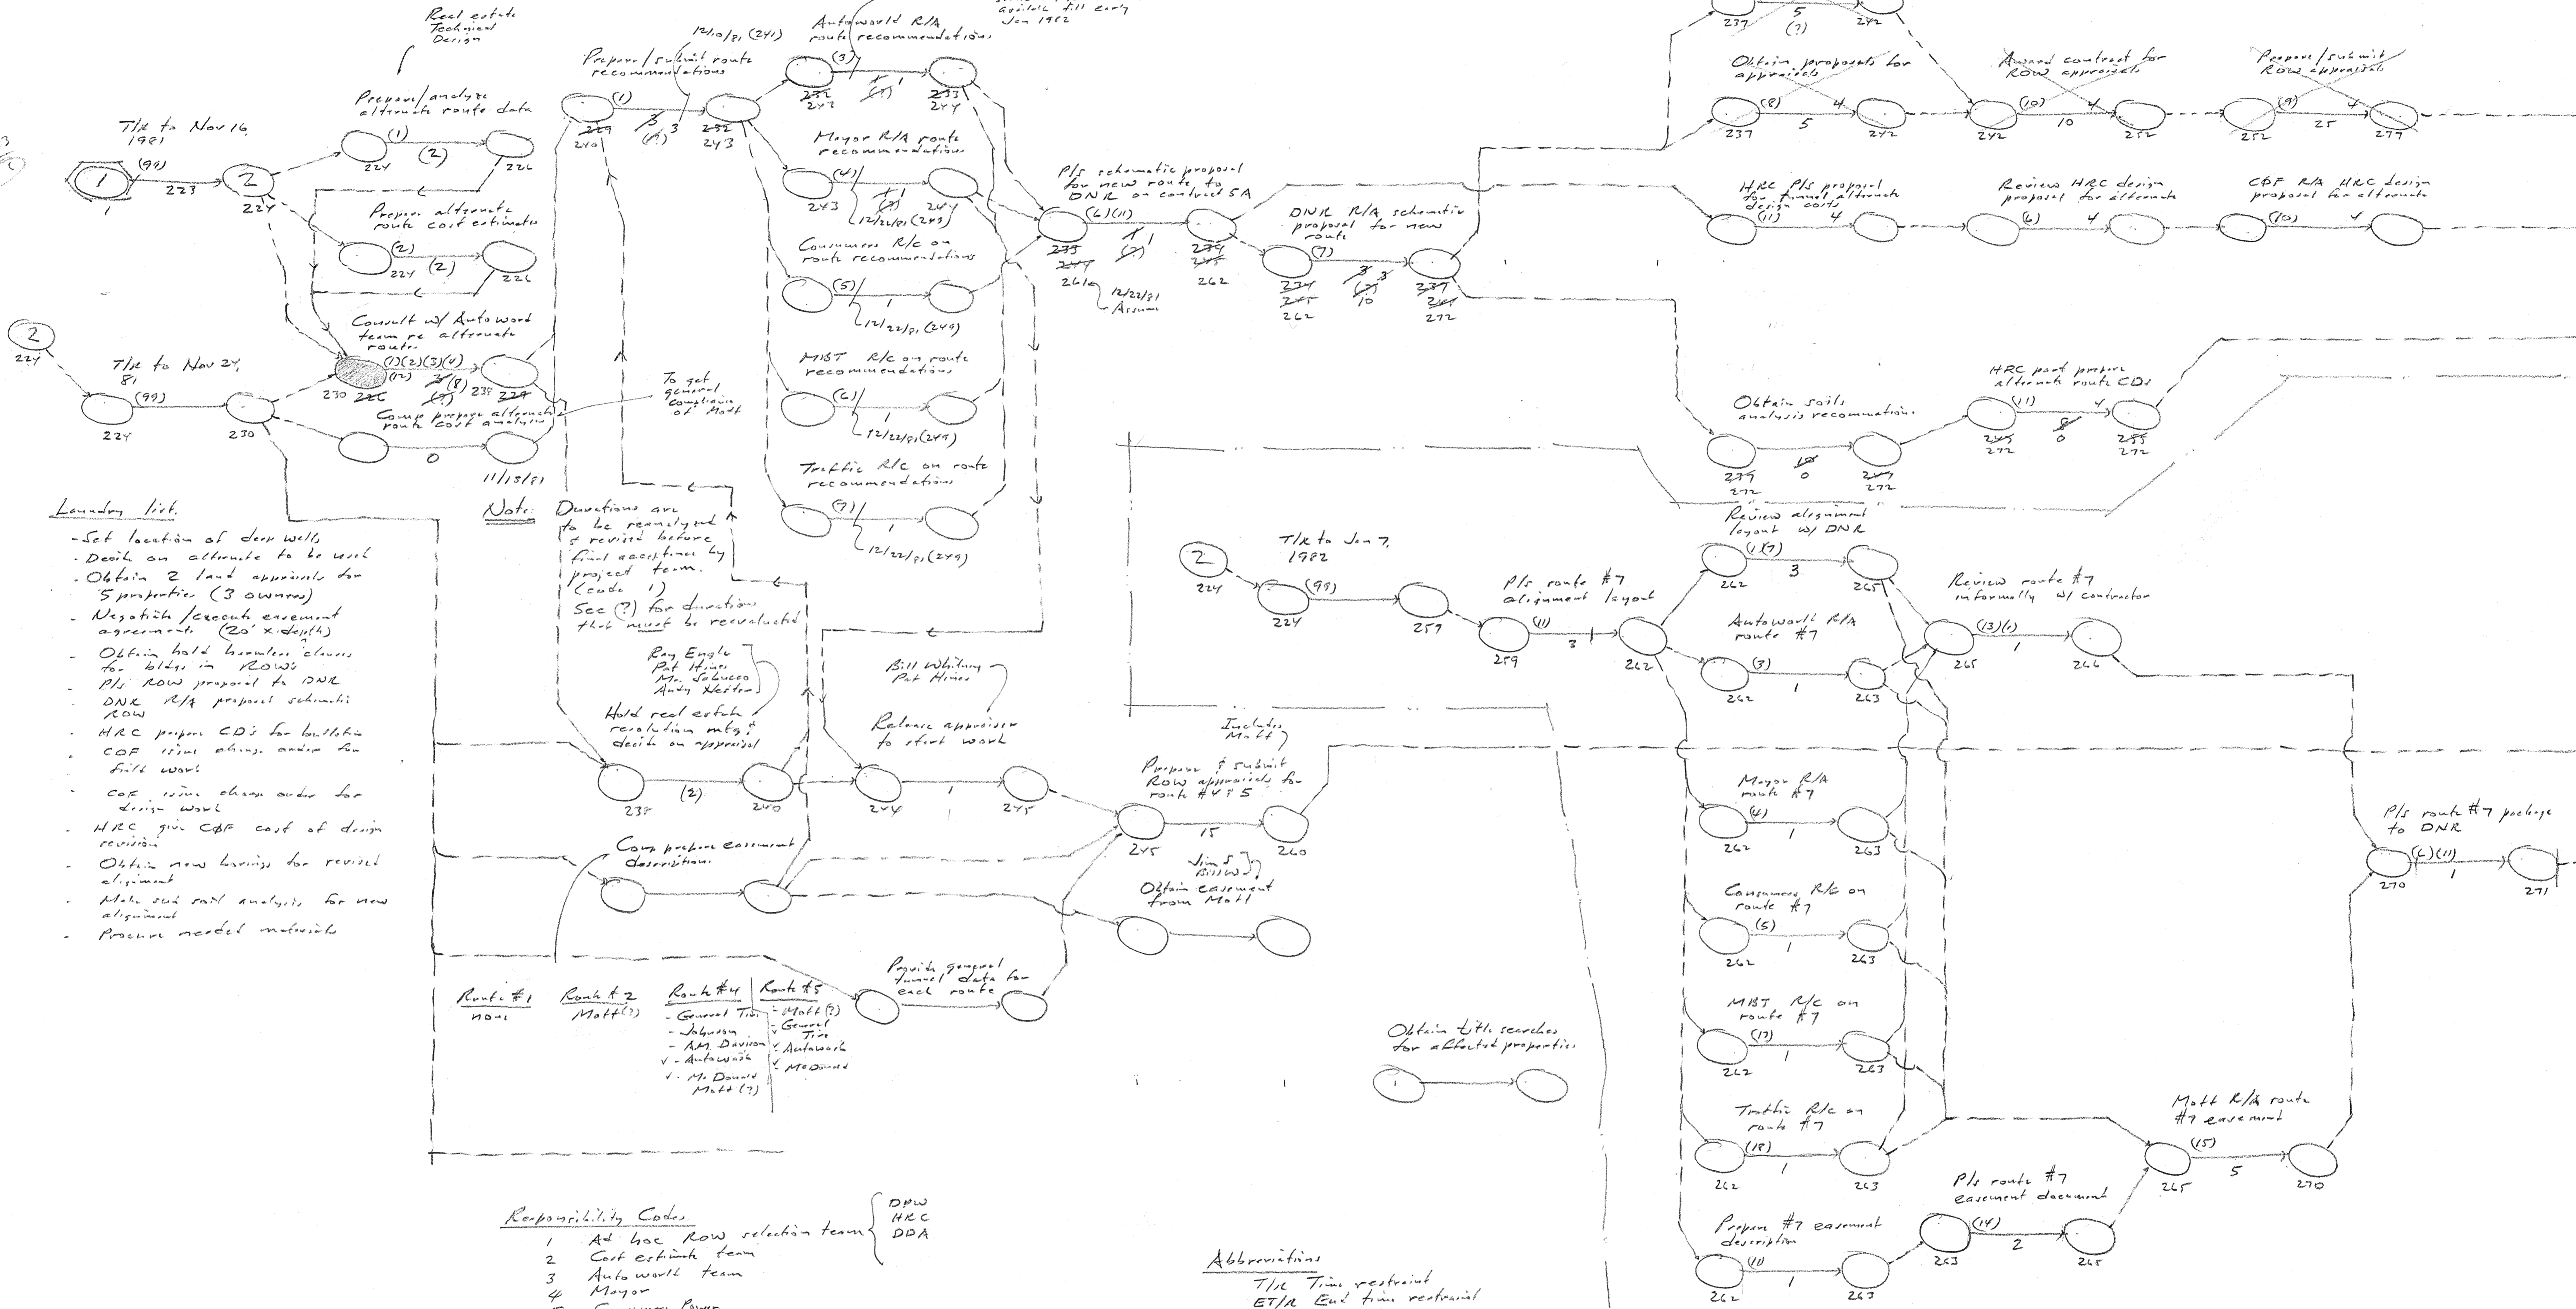

- Laundry list**
- Set location of deep wells
 - Decide on alternate to be used
 - Obtain 2 land appraisals for 5 properties (3 owners)
 - Negotiate/execute easement agreements (20' x depth)
 - Obtain hold basement claims for bldgs in ROWs
 - P/E ROW proposal to DNR
 - DNR R/A proposal schematic ROW
 - HRC prepare CD's for bulletin
 - COP issue align. order for fill work
 - COP issue chain order for design work
 - HRC give COP cost of design revision
 - Obtain new bearings for revised alignment
 - Make out soil analysis for new alignment
 - Prepare model materials

Note: Directions are to be reanalyzed & revised before final acquisition by project team. (code 1)
See (?) for directions PLB must be reevaluated

- | Route #1 | Route #2 | Route #4 | Route #5 |
|----------|----------|---|--|
| no one | Matt(?) | - General Tib
- Johnson
- Am Davison
- Auto word
- M. Downe
- Matt (?) | - Mott (?)
- General Tib
- Am Davison
- Auto word
- M. Downe
- Matt (?) |

- Responsibility Codes**
- 1 At hoc ROW selection team
 - 2 Cost estimate team
 - 3 Auto word team
 - 4 Mayor
 - 5 Consumers Power
 - 17 Michigan Bell
 - 18 Traffic dept.
 - C DPW
 - 7 DNR
 - 8 Jerry Hungerford
 - 9 Appraisers
 - 10 City of Flint
 - 11 Hankel, Rath, Clark
 - 12 SSOE
 - 13 Greenfield
 - 14 Pat Hines
 - 15 Mott Foundation
 - 16 City council
 - 17
 - 18

- Abbreviations**
- T/R Time restraint
 - ET/R End time restraint
 - EOP End of project
 - R/C Review & comment
 - R/A Review & approve
 - P/E Prepare & submit
 - CD Contract documents
 - C&F City of Flint
 - ROW Right of way
 - DNR Dept. of Natural Resources

MONITORING RECORD			ISSUE RECORD	
DATE	DATE	DATE	ISSUE No.	DATE
			1	Nov 13, 81
			2	Nov 24, 81
			3	Dec 14, 81
			4	Dec 22, 81
			5	JAN 7, 82

Reserved Note No.

LN
HN

**NETWORK MODEL FOR
TUNNEL ROUTE ALTERNATE
ACTION
FLINT, MICHIGAN**

RALPH J. STEPHENSON, P.E.
15064 WARWICK ROAD
DETROIT, MICHIGAN 48223
CONSULTANT PH 273-5026

#093
#085
59
