


314
219
75

Subject code
APV MBL
AWC MBT
CAD PAS
CBE PAS
CP PAS
MST PAS
CTU RAO
DPW RAO
DCD RAO

Mail copies to
Ron Campbell &
John H. Gentry

Leadwork List

- Obtain preliminary CBE approval on bridge
- Prepare bridge CDD
- Obtain final CBE approval on bridge CDD
- Comp. P/S design development package
- DCD R/A DD package
- Rob Collins R/A DD package
- DPW R/A DD package
- CP R/C DD package
- MST R/C DD package
- Comcast R/L DD package
- P/S CDD
- DCD R/A CDD
- DPW R/A CDD
- MST P/S proposal for utility work
- CP P/S proposal for utility work
- Comcast P/S proposal for utility work
- CBE R/A CP proposal
- CBE R/A MST proposal
- CBE R/A Comcast proposal
- THA revise CDD's as part of utility CDD's for proposals
- P/S proposal for PASE work
- Review proposals & select contractor
- Execute contract for PASE work
- Hold preconstruction mtg
- Mobilize & move on site

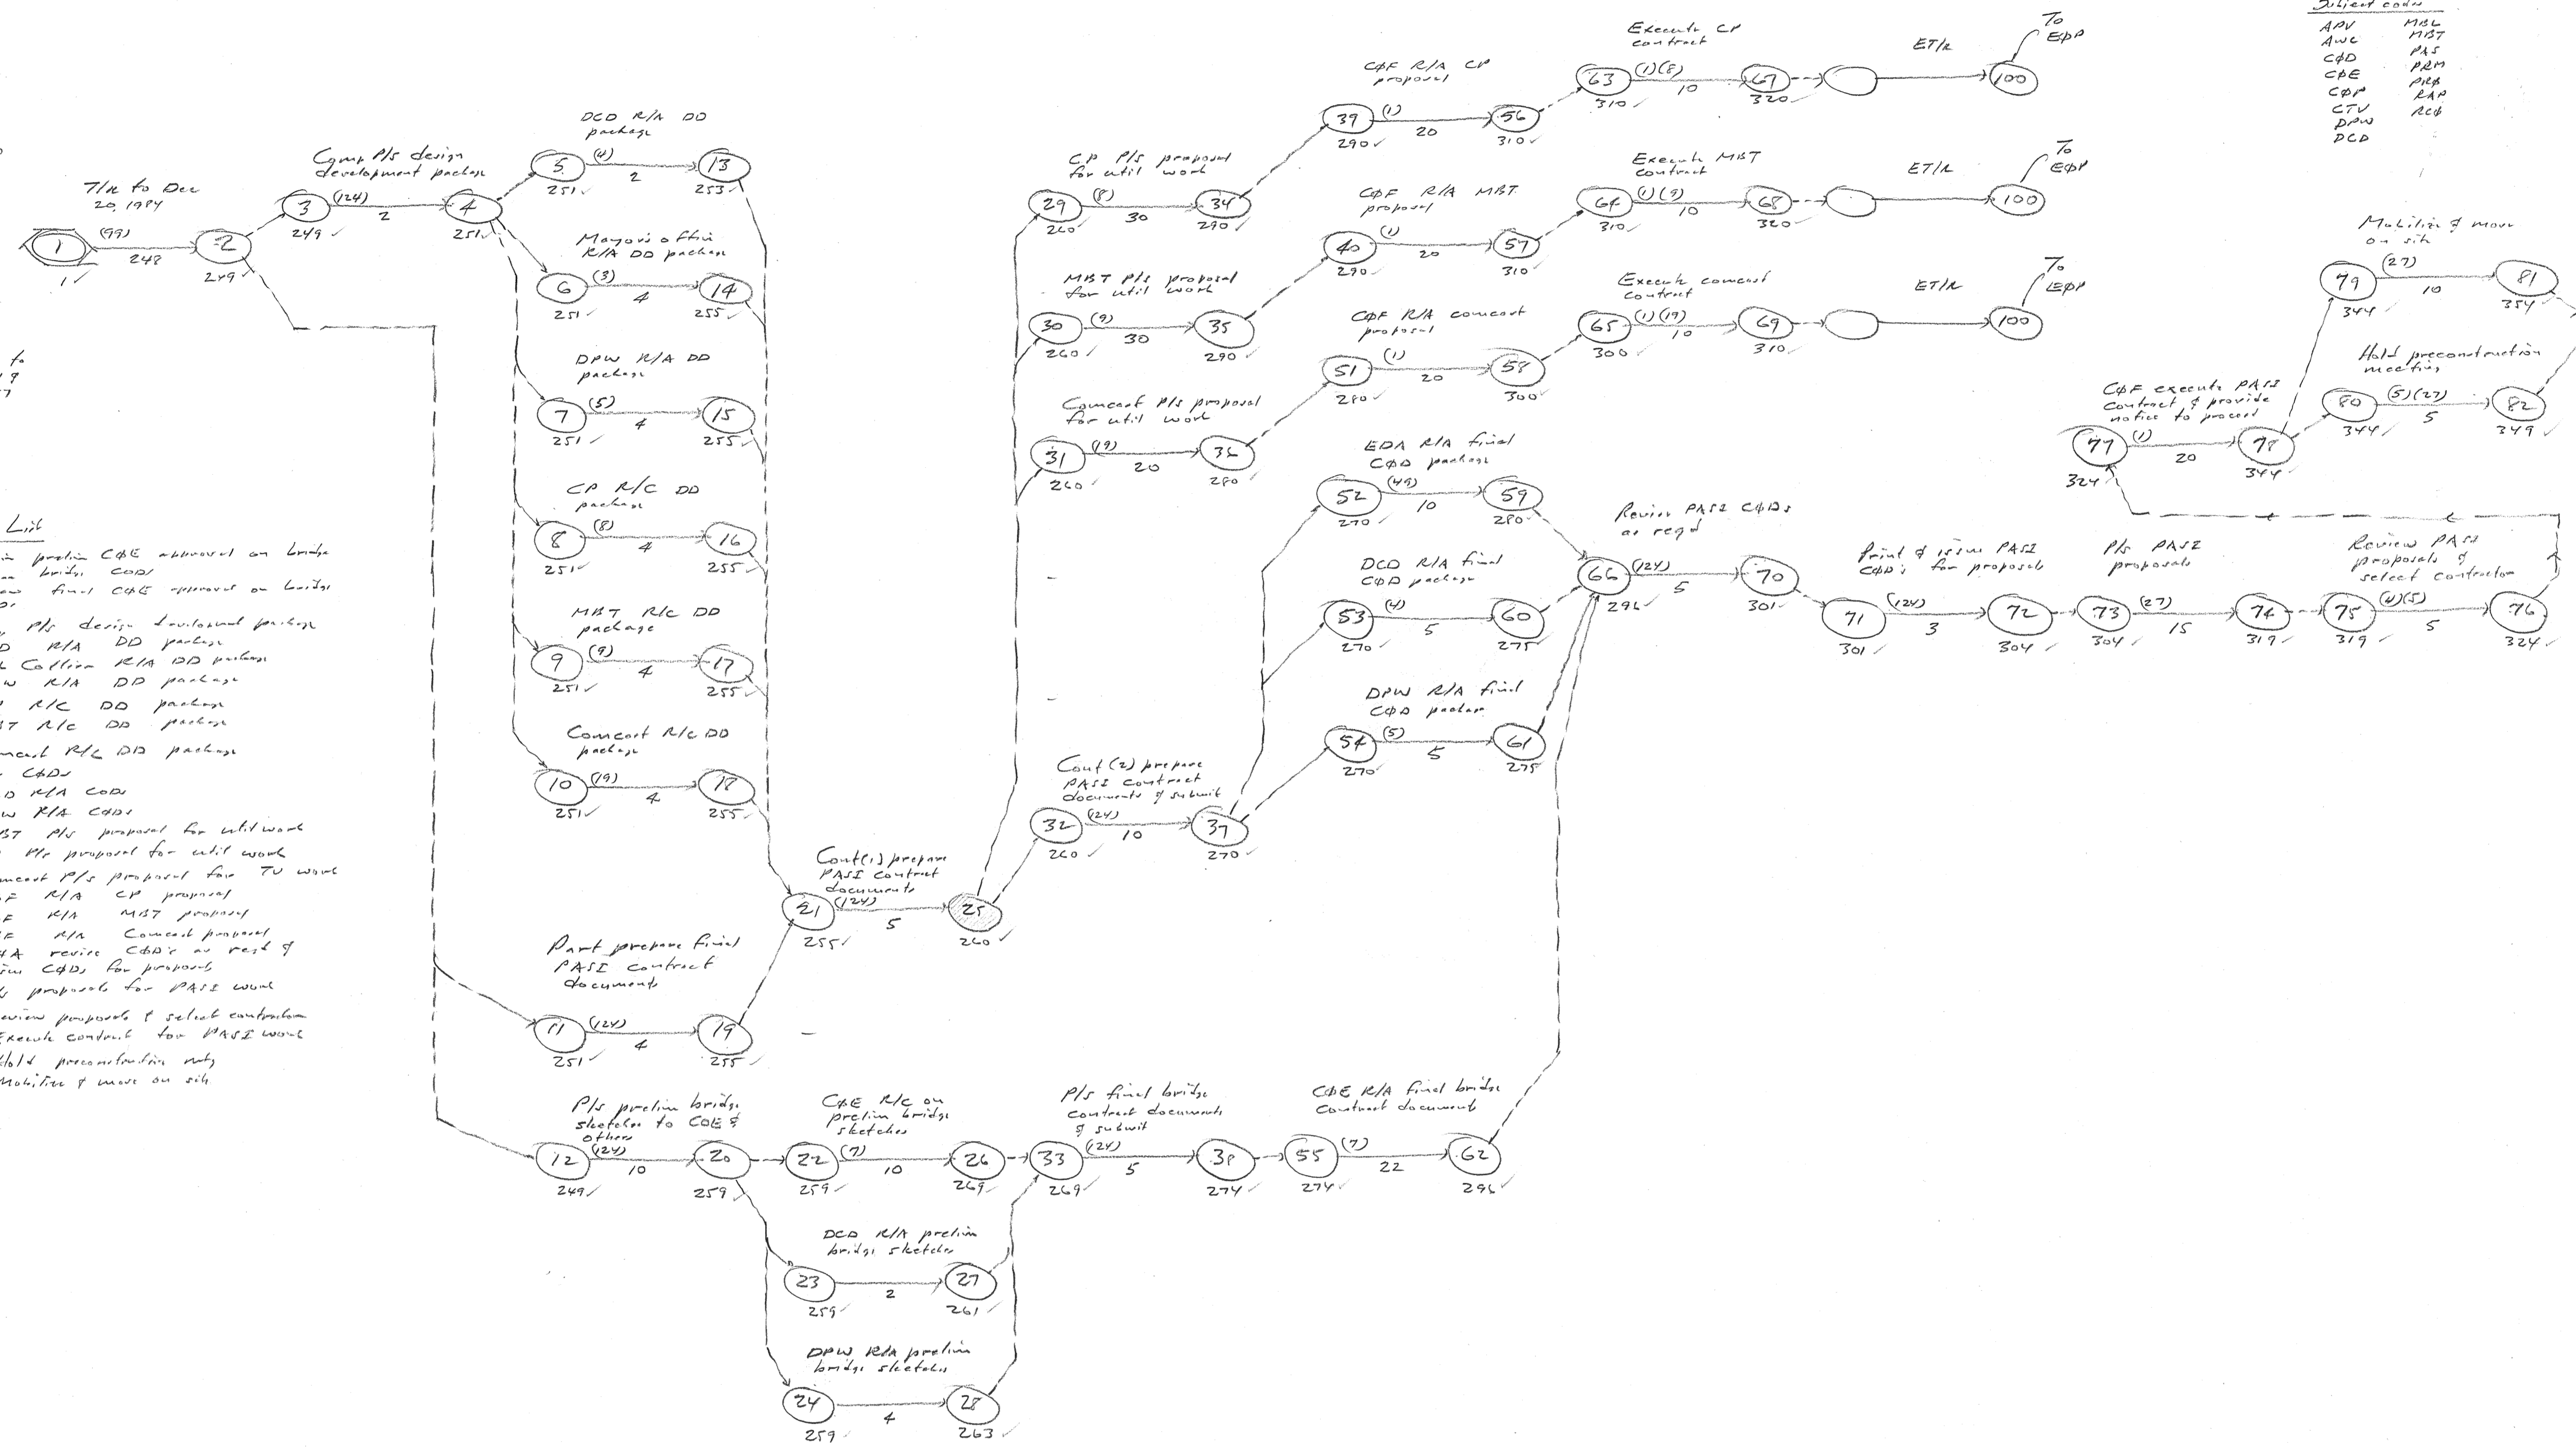

PASE DESIGN WORK

Responsibility Codes

- 1 City of Flint
- 3 Mayor's office
- 4 DCD
- 5 DPW
- 7 Corps of Engineers
- 8 Consumers Power
- 9 Michigan Bell
- 19 Comcast
- 27 Contractors
- 49 EDA
- 124 THA

Abbreviations

- TR Time restraint
- PS Prepare & submit
- DD Design development
- R/A Review & approval
- R/C Review & comment
- CP Consumers Power
- MST Michigan Bell Telephone
- CBE Corps of Engineers
- PASE Public area site improvements
- CDD's Contract documents
- CAF City of Flint

MONITORING RECORD			ISSUE RECORD	
DATE	DATE	DATE	ISSUE No.	DATE
			1	DEC 20, 97

Reserved Node Nos.

- 41 46 83 88 93
- 42 47 84 89 94
- 43 48 85 90 95
- 44 49 86 91 96
- 45 50 87 92 97
- 98
- 99

LN 1
HW 100

NETWORK MODEL FOR
CARRIAGE TOWN PROJECT
FLINT, MICHIGAN

RALPH J. STEPHENSON, P.E.
15064 WARWICK ROAD
DETROIT, MICHIGAN 48223
CONSULTANT PH 273-5026

157
